


## TransNet Quarterly Status Report April 2025 – June 2025

Data as of 06/30/2025

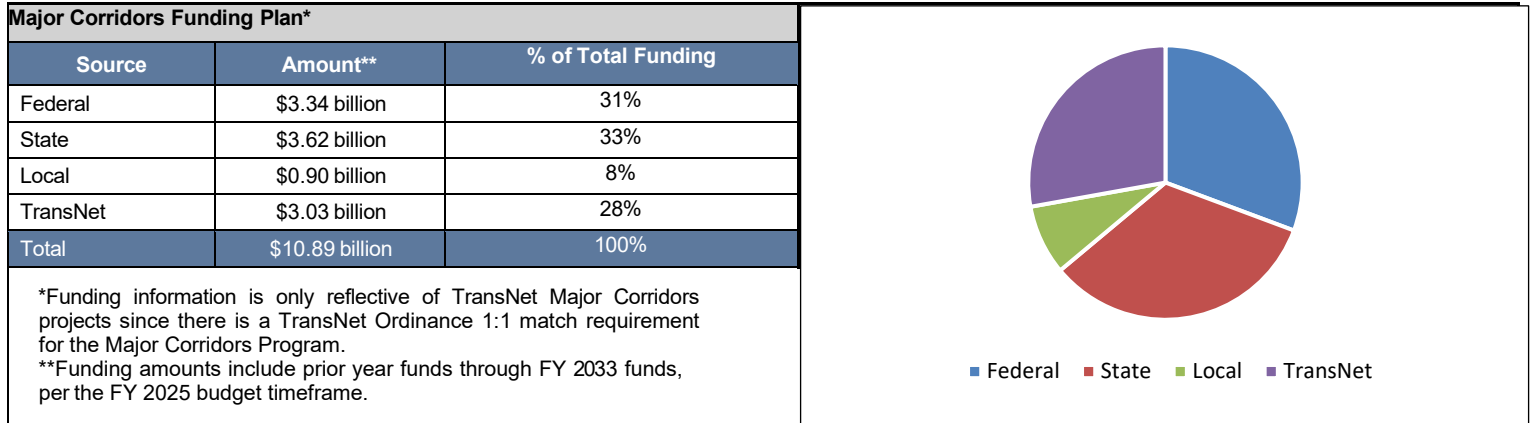


Major Corridors & Bikeway Milestones		Milestones marked as A indicate an actualized event. Milestones marked as X indicate a planned event.							
Segment	FY 2025 Baseline Date***	Milestone	2025 Apr	2025 May	2025 Jun	2025 Jul	2025 Aug	2025 Sep	
<b>I-805 Projects</b>									
I-805 North Auxiliary Lanes (CIP-1280516)	Aug 2025	OTP					X		
<b>I-5 North Corridor</b>									
SR 56 HOV Lanes (CIP-1200513)	May 2025	OTP				A			
<b>Orange-Blue Line Corridor</b>									
Blue Line Railway Signal Improvements (CIP-1210021)	Jan 2025	BEGIN						X	
Low-Floor Light Rail Transit Vehicles (CIP-1210090)	May 2025	OTP		A					
<b>SR 78/SPRINTER Projects</b>									
I-15/SR 78 HOV Connectors (CIP-1207802)	Dec 2024	DED		A					
<b>Regional Bikeway Projects</b>									
Uptown Bikeways: Washington Street and Mission Valley Bikeway (CIP-1223084)	Feb 2025	BEGIN		A					
North Park/Mid-City Bikeways: University Bikeway (CIP-1223081)	Dec 2024	BEGIN						X	

**Schedule Milestones:**  
**DED** represents the release of the Draft Environmental Document to the public for comment, or when the document is sent to the lead federal agency for review.  
**FED** represents the signing of the Final Environmental Document by approving agency  
**ADVERTISE** represents the completion of the project design and advertisement of the construction contract. Before advertisement, all environmental permits have been acquired, right of way has been certified, and the plans, specifications, and engineer's estimate has been completed.  
**BEGIN** represents the beginning of construction initiated by the Notice to Proceed.  
**OPEN** represents the opening of the constructed facility for its intended use.  
**CON COMPLETE** represents the completion of all construction and most of project closeout items for the project. This includes, but is not limited to: construction contract acceptance, complete plant establishment/landscaping, final inspection, closure of task orders, and all claims settled.


\*\*\*FY 2025 Baseline Date refers to the baseline milestone completion date that was set in the FY 2025 Program Budget.

**TransNet Quarterly Status Report  
April 2025 – June 2025**

**Regional Bikeway Monthly Expenditures**

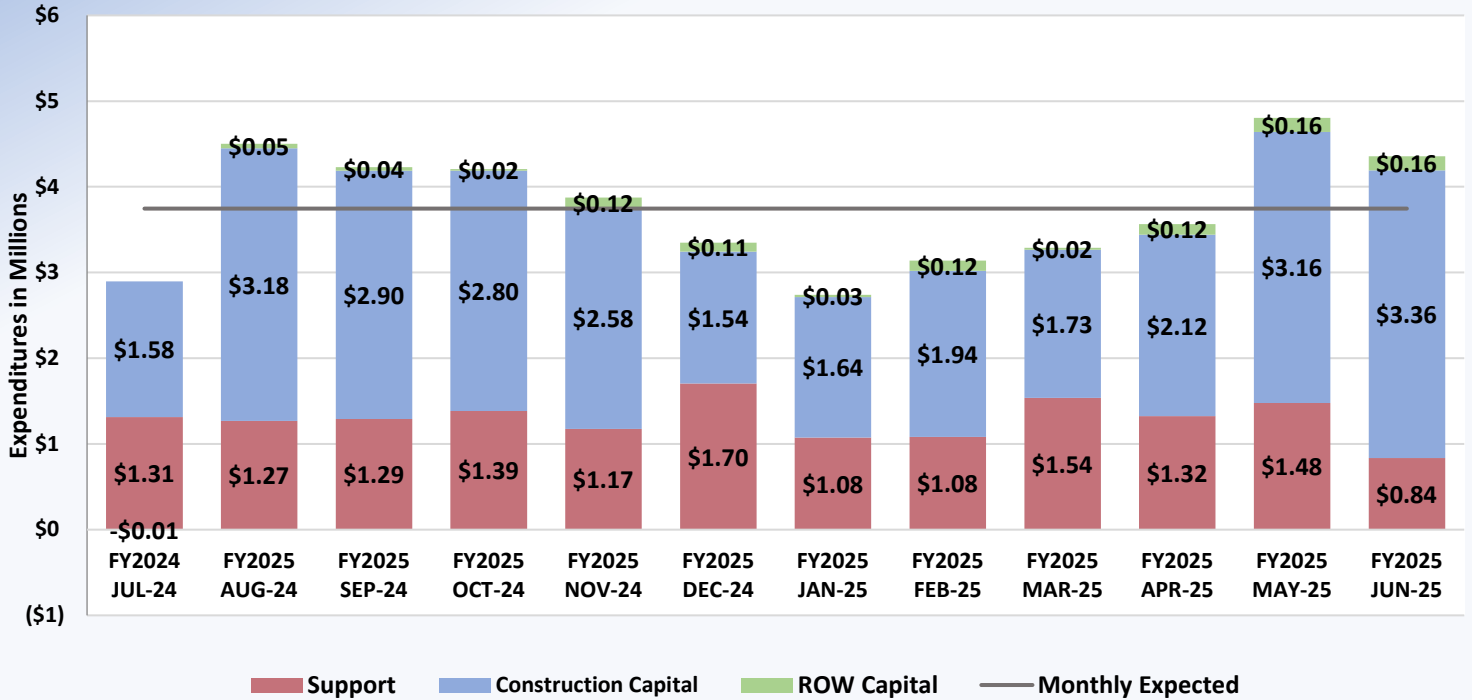

**Major Corridor Monthly Expenditures**

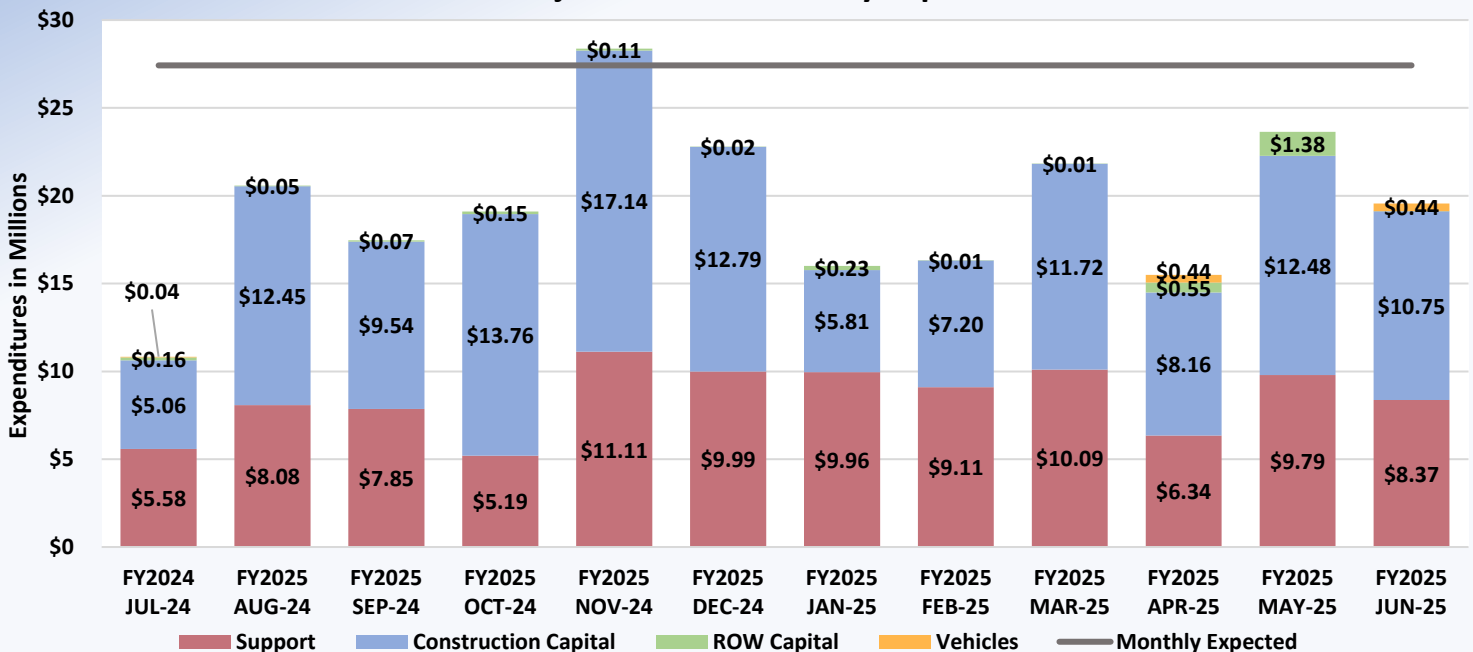


\* Support - Includes Administration, Design, Environmental, Right of Way Support, Construction Management, Legal Services, and Communications.


\* Monthly expenditures are reported on the 20th of each month.

**TransNet Quarterly Status Report  
April 2025 – June 2025**

**Regional Bikeway Yearly Expenditures**

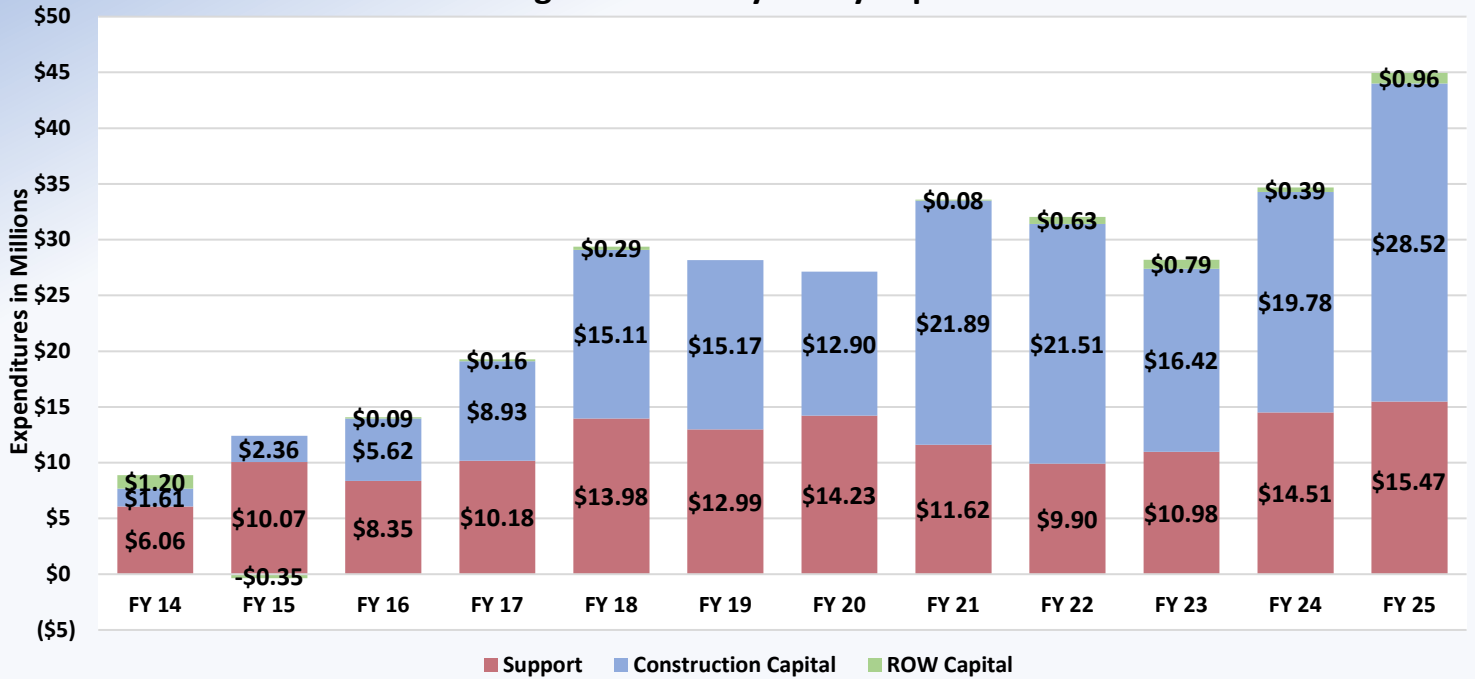


**Major Corridor Yearly Expenditures**

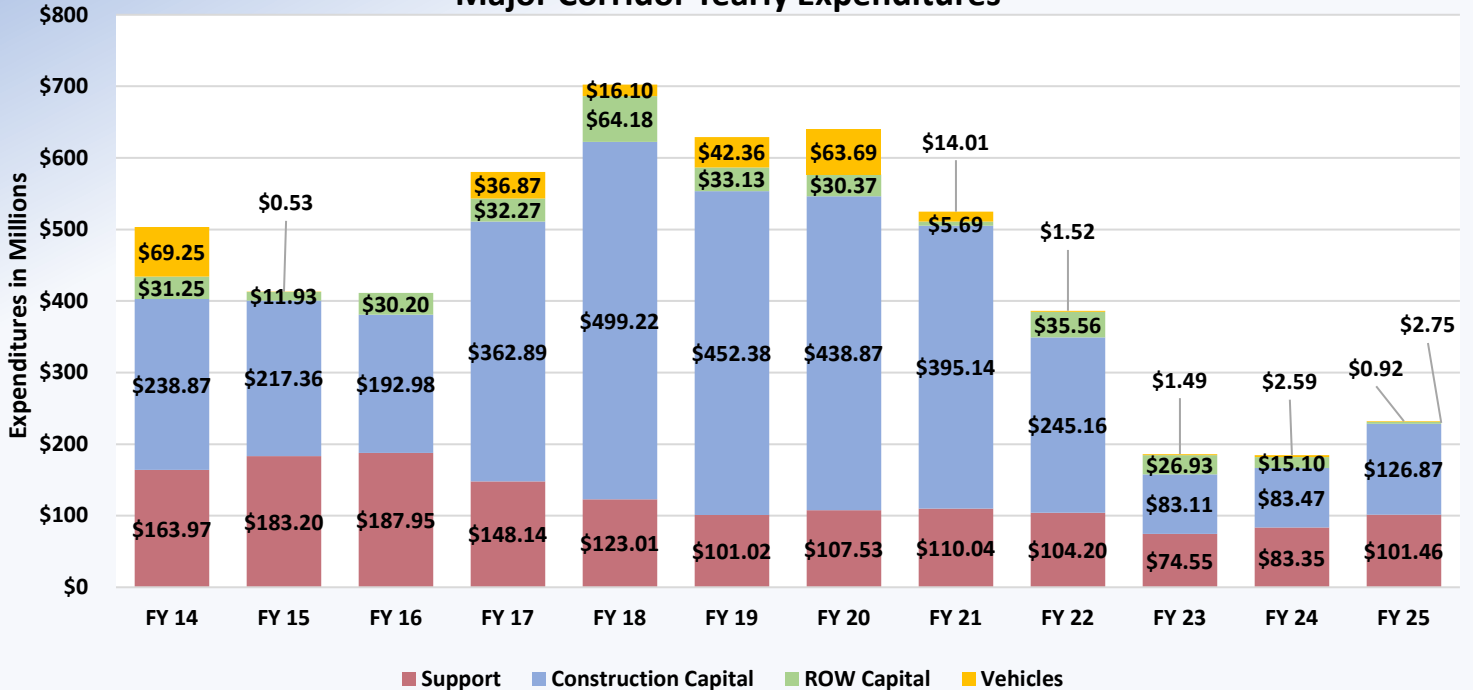

\* Support - Includes Administration, Design, Environmental, Right of Way Support, Construction Management, Legal Services, and Communications.

\* Monthly expenditures are reported on the 20th of each month.

ENR Cost Indexes in Los Angeles 2005 - 2025  
[https://www.enr.com/economics/historical\\_indices/losangeles](https://www.enr.com/economics/historical_indices/losangeles)

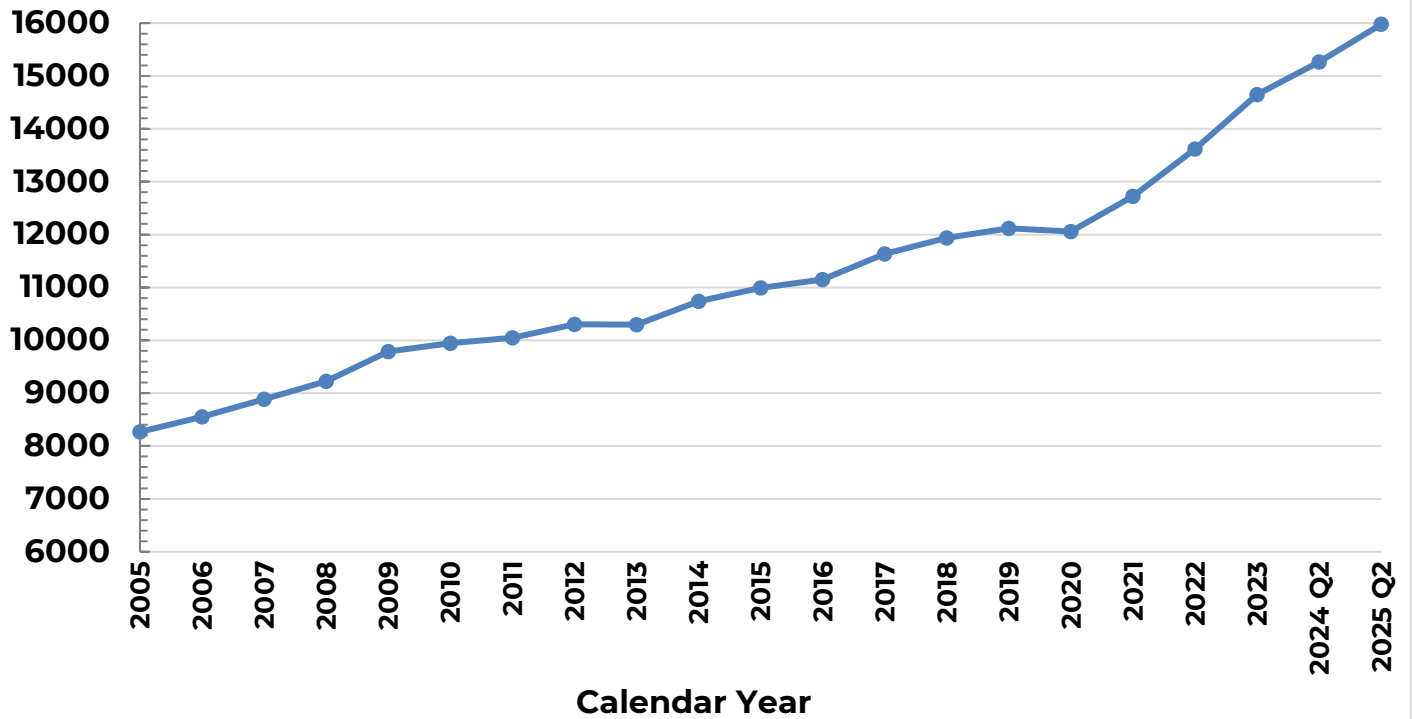

Caltrans Construction Cost Index 2005 - 2025

